
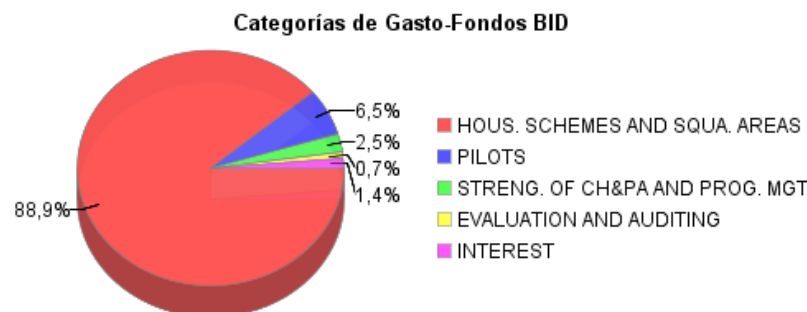
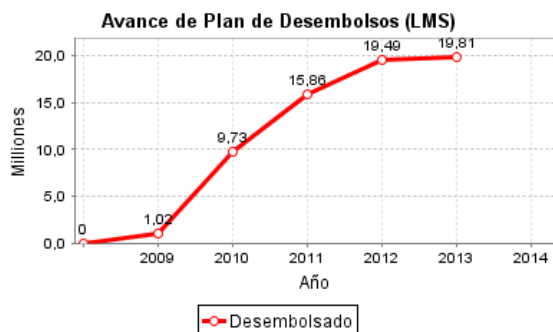


## Informe Resumido


Datos Básicos del Proyecto		Fondos Disponibles (US\$)		Costo total y Fuente	
Agencia Ejecutora (AE):	CENTRAL HOUSING PLANNING AUTHORITY	Monto Aprobado Actual:	27.900.000,00	BID Original:	27.900.000,00
Sector:	URBAN DEVELOPMENT AND HOUSING-HOUSING	Monto Desembolsado a la fecha:	19.805.299,17	Actual BID:	27.900.000,00
Número(s) de Préstamo:	2102/BL-GY	% Desembolsado:	70,99	Pari-passu:	100,00
Etapas:	Approved	Saldo:	8.094.700,83	Co-financiamiento/País:	
Tipo de Operación:	INV - Inversión			Estimado Original:	27.900.000,00
Operación(es) Relacionada(s):	GY-P1007, GY-T1059			Período de Amortización (meses):	288
Subtipo de Operación:	ESP - Inversión Específica				

Categoría de Impacto Ambiental y Social del Proyecto	Reformulación	Validación
Categoría de Impacto Ambiental y Social del Proyecto: B	( ) ¿El objetivo (s) del proyecto fue reformulado?	Validado por el Jefe de División: 16-abr-2013 Validado por Representante de País:

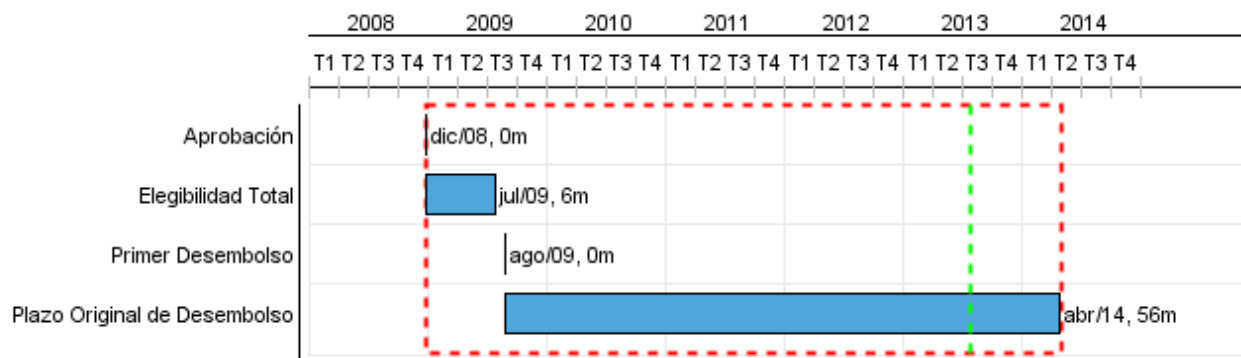

**Progreso Acumulado al 2012**

**Progreso Acumulado**

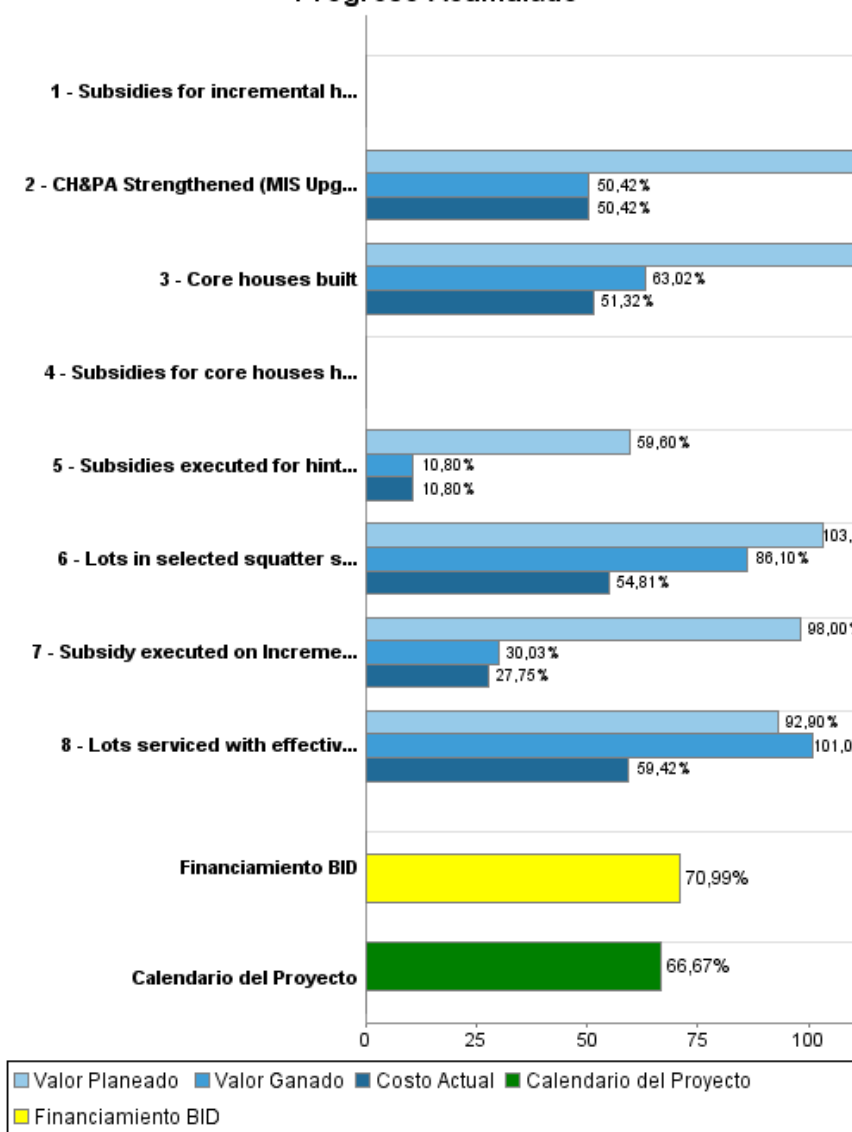

## Resultados

**Resultado:** Access to housing improved

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2013	Fin de Proyecto
Low income families occupy dwellings that at least meet the following minimum standards: 312 sq.ft. with septic tank, water, power connection, and located on land with access.	dwellings	3.880,00	2008	P	13.580,00	13.580,00
				A		

**Productos: Progreso Físico y Financiero Anual 2012**

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
<b>Comp. I New sites with services that consolidated existing housing schemes and that upgraded squatter areas developed. The execution of the plans is related to the site's upgrading.</b>									
Lots serviced with effective drainage, water, and electrical connections.	Lots	2.857,00	1.690,00		8.467,00	3.000.000,00	2.717.000,00		19.300.000,00
Core houses built	Hogares	100,00	76,00		400,00	1.000.000,00	640.000,00		2.200.000,00
Lots in selected squatter settlement upgraded, including paving of access street, drainage, septic tanks, and water supply	Hogares	550,00			973,00	122.781,00	85.000,00		3.300.000,00
Subsidies for core houses handed over to female headed households	subsidies		48,00				87.000,00		
<b>Comp. II Pilots that attended issues of affordability and sustainability implemented</b>									
Subsidy executed on Incremental housing	Subsidies	150,00	112,00		400,00	100.000,00	111.000,00		400.000,00
Subsidies for incremental housing disbursed to female headed households	Subsidies		53,00				56.000,00		
Subsidies executed for hinterland (houses and roof)	Subsidies		75,00		200,00		108.000,00		1.000.000,00
<b>Comp. III Central Housing &amp; Planning Authority Strengthened (CH&amp;PA)</b>									
CH&PA Strengthened (MIS Upgraded, Housing Policy designed, Strategic planning developed, CH&PA regional housing offices strengthened).	Office				1,00	95.695,00	154.000,00		430.000,00
Program Management & Evaluation	N/A					173.286,94	33.000,00		470.000,00
<b>Financial Expenses</b>									
FIV ("Fondo de Inspección y Vigilancia") (1%) & Interest (2%)	N/A					53.000,00			265.000,00
<b>TOTAL</b>						<b>4.544.762,94</b>	<b>3.991.000,00</b>		<b>27.365.000,00</b>
