
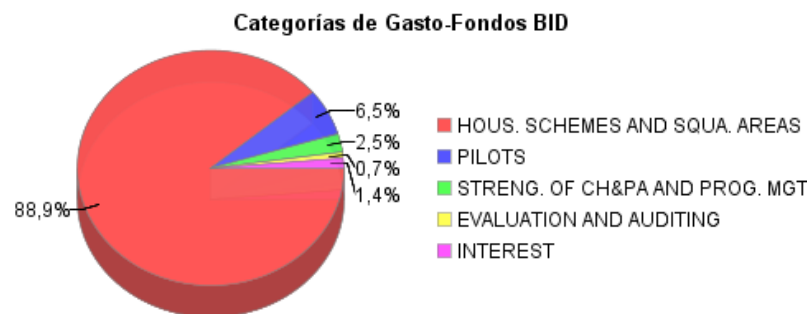
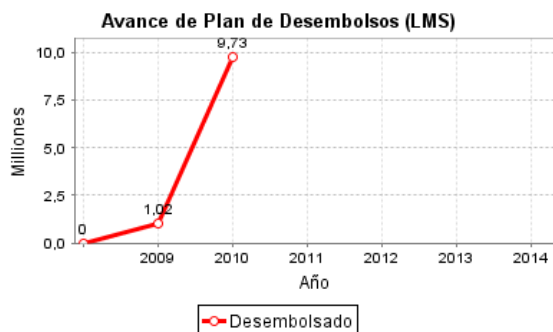


Informe Resumido


Datos Básicos del Proyecto		Fondos Disponibles (US\$)		Costo total y Fuente	
Agencia Ejecutora (AE):	CENTRAL HOUSING PLANNING AUTHORITY	Monto Aprobado Actual:	27.900.000,00	BID Original:	27.900.000,00
Sector:	URBAN DEVELOPMENT AND HOUSING-HOUSING	Monto Desembolsado a la fecha:	10.680.754,80	Actual BID:	27.900.000,00
Número(s) de Préstamo:	2102/BL-GY	% Desembolsado:	38,28	Pari-passu:	100,00
Etapas:	Approved	Saldo:	17.219.245,20	Co-financiamiento/País:	
Tipo de Operación:	INV - Inversión			Estimado Original:	27.900.000,00
Operación(es) Relacionada(s):	GY-P1007, GY-T1059			Período de Amortización (meses):	288
Subtipo de Operación:	ESP - Inversión Específica				

Categoría de Impacto Ambiental y Social del Proyecto	Reformulación	Validación
Categoría de Impacto Ambiental y Social del Proyecto: B	() ¿El objetivo (s) del proyecto fue reformulado?	Validado por el Jefe de División: Apr 7, 2011 Validado por Representante de País: Apr 13, 2011

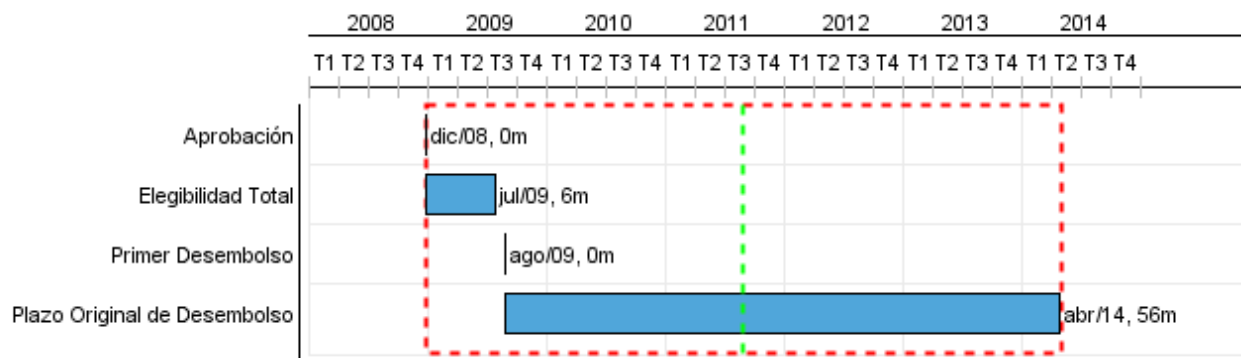

Progreso Acumulado al 2010

Progreso Acumulado

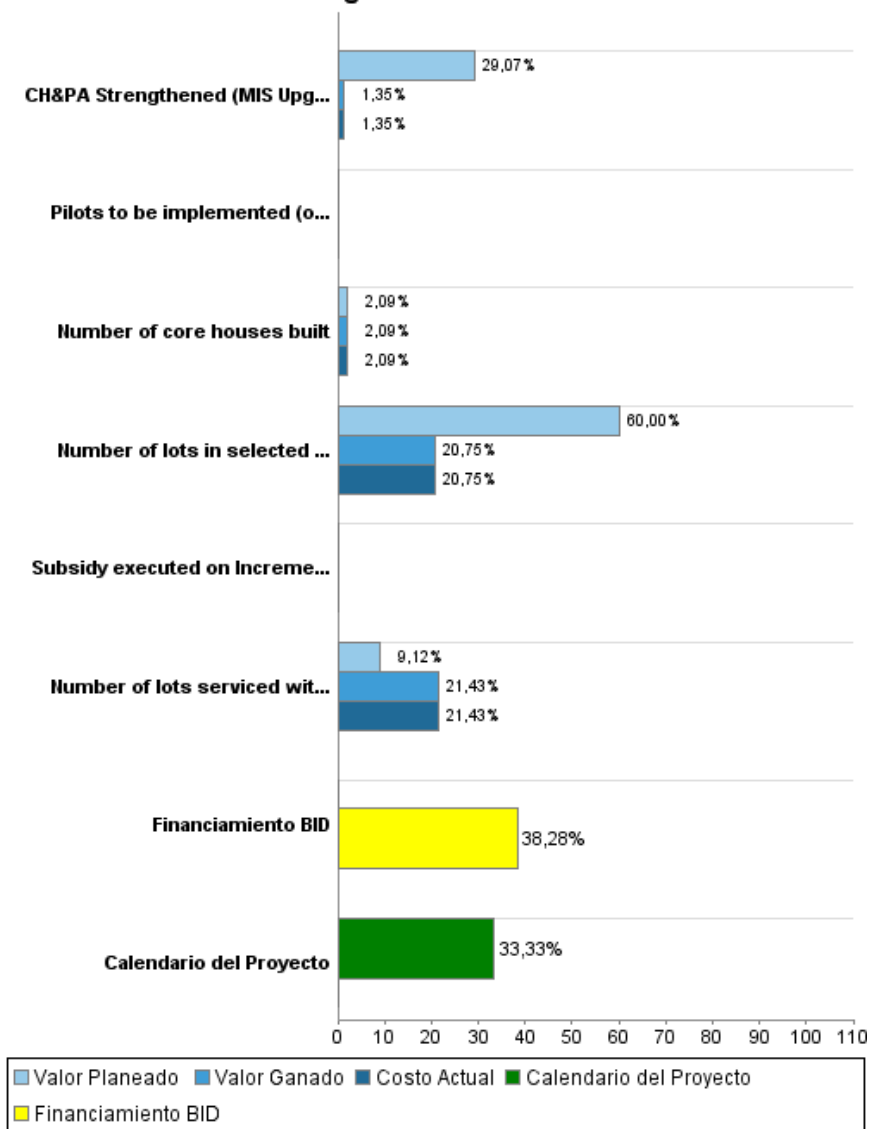

Resultados

Resultado: Access to housing improved

Indicador	Unidad de Medida	Línea de base	Año Línea de base		2013	Fin de Proyecto
Low income families occupy dwellings that at least meet the following minimum standards: 312 sq.ft. with septic tank, water, power connection, and located on land with access.	dwellings	3.880,00	2008	P	13.580,00	13.580,00
				A		

Productos: Progreso Físico y Financiero Anual 2010

Descripción	Unidad de medida	Físico				Financiero			
		Planeado	Actual	Unidades Acumuladas	Unidades FDP	Planeado	Actual	Costos Acumulados	Costos FDP
Comp. I New sites with services that consolidated existing housing schemes and that upgraded squatter areas developed. The execution of the plans is related to the site's upgrading.									
Number of lots serviced with effective drainage, water, and electrical connections.	Lots		280,00		9.071,00	1.080.003,00	3.456.729,00		19.300.000,00
Number of core houses built	Core houses				400,00		46.043,00		2.200.000,00
Number of lots in selected squatter settlement upgraded, including paving of access street, drainage, septic tanks, and water supply	Lots		211,00		1.290,00	1.980.000,00	684.684,00		3.300.000,00
Comp. II Pilots that attended issues of affordability and sustainability implemented									
Subsidy executed on Incremental housing	Subsidies				400,00				400.000,00
Pilots to be implemented (one for the hinterland and one to foster PPP)	Subsidies								1.535.000,00
Comp. III Central Housing & Planning Authority Strengthened (CH&PA)									
CH&PA Strengthened (MIS Upgraded, Housing Policy designed, Strategic planning developed, CH&PA regional housing offices strengthened).	System				1,00	125.000,00	5.805,00		430.000,00
Financial Expenses									
TOTAL						3.185.003,00	4.193.261,00		27.165.000,00
